



EVALUETOR

PROPOSAL

For Canopy

This document is a proposal for the implementations and usage of Evalueter for the Canopy organisation.

Contact Information:

Steven Visser

Steven.Visser@senority.nl

Tel: +31 6 31003495

Table of Content

1. MANAGEMENT SUMMARY.....	3
2. A PHASED APPROACH.	5
2.1 Step-1:	5
2.2 Step-2:	6
2.3 Step-3:	6
3. STEP-1: PROGRAM IMPLEMENTATION STRUCTURE.....	7
3.1 Planning of Step-1.	7
3.2 Set-up Canopy Evalueter.	7
3.3 Preparations.	8
3.4 Process Support.	8
3.5 Integration	10
3.6 Implementation Support.....	10
3.7 Program Governance Structure.....	10
4. STEP-1 TIME ESTIMATES AND ASSUMPTIONS.	12
4.1 Estimating and costing assumptions.	12
4.2 Progress reporting and hour administration.	13
4.3 Step-1 Time and cost estimates per activity.	13
4.4 Consideration for the number of Canopy Evalueter subscriptions	13
5. EVALUETOR USER SUBSCRIPTION FEES AND RATES.	15
5.1 Evalueter Cloud Services.	15
5.2 Storage Fees.....	15
5.3 Support and Development Services.	15
6. APPENDIX A - SHORT DESCRIPTION EVALUETOR FUNCTIONALITY.....	16
6.1 Relationship Management.	16

6.2	Contract Management.	16
6.3	Service Management.	17
6.4	Improvement Management.	17
6.5	Risk Management.	17
6.6	Opportunity Management.	18
6.7	System Administration.	18
6.8	Management Reporting.	18

Related documents attached as separate files:

Appendix B – 20140908 Evaluetor General Terms and Conditions for Canopy v1.0

Appendix C -- 20140908 Draft Evaluetor User Agreement EUA for Canopy v1.0

Appendix D -- 20141015 Requirements modelling Canopy Evaluetor

1. Management Summary.

Canopy is actively building the European Cloud leader which is positioned to serve multinational customers globally. Leveraging their significant resources to ensure they deliver on promise to create tangible business value for their clients and stakeholders. Doing this at the competitive level that differentiates Cloud from traditional service provision requires to run the Canopy organisation as a tight ship. The foundation enabling such a client relationship is a well organised delivery organisation that is aware of all its obligations to the client(s). Which is timely alerted if set objective are at risk.

The objective of this Evaluetor implementation is to bridge the differences of the Client oriented Atos processes and the product orientation typical for a cloud company like Canopy. By entering the basic information received from the various sources into the Evaluetor system instead of in excel spreadsheets the challenge of assuring compliance to the multitude of requirements will be dramatically simplified. Evaluetor will automate the checks and balances in real time and structure the information in dashboard, reports and alerts tuned toward the different disciplines in the Canopy organisation. This will eliminate the linear growing workload on the CDM's allowing more focus on client needs and optimising contract and product performance.

After the successful Proof of Concept (PoC) where the Senority Team worked with Koos van den Berge to demonstrate the fit for purpose of Evaluetor for the majority of Canopy's current processes (See Appendix D: "20141015 Requirements modelling Canopy Evaluetor"), Senority is pleased to present its proposal for the implementation and provisioning of Evaluetor to Canopy. Evaluetor is a cloud based contract and relationship management solution that helps companies to improve their client focus and operational efficiencies. By better managing client, contract and internal commitments client satisfaction will improve. This will result in better returns on contracted business, higher renewal rates, and more add-on business.

The essential information from the Client Pack will be captured in Evaluetor and the monitoring and management of both the delivery (SLA) and customer care (CSAT & NPS) status as well as the financial and billing (DSO) information is now available in real time to the different Canopy organisations and geographies. These business indicators enable transparent communication of achieved benefits and a continuous improvement process for the Canopy client. Senority will help implement a contract management process that allows Canopy to constantly monitor the execution of contract commitments and the transparent interaction with the client facilitating existing governance structures.

We propose a structured and phased approach that is sensitive to the current workload of the people in the organisation and the organisational position of Canopy in the Atos organisation. We recognize the following main processes that need to be supported, and propose a phased implementation per main process.




Figure 1 Canopy's main processes

The Senority proposal includes the implementation cost and subscriptions to the Evaluetor service. Next to the process support implementations, Senority will provide change management support to assist the CDM team in operationalising the Evaluetor tooling within the Canopy organisation and obtain maximum benefits from the implementation. Implementation is proposed on a time and material basis. Senority has provided estimates for the expected implementation cost. Actual implementation cost will depend to a large extent on the level of commitment, involvement and support that Canopy will provide during the implementation phase.

Given the fact that initially the number of Evaluetor user subscriptions will be limited to Canopy CDM staff only, who are organising the tasks and information we offer a 50 user subscription for € 5.000,- per month. Additional user subscriptions can be made available for € 75, - per month.

2. A phased approach.

Senority is pleased to present our approach for the implementation and use of Senority's Contract Management cloud service "Evaluator". Being sensitive for the priorities within Canopy today we advise a stepped approach, recognising the following steps:

1. Implement the framework to support the main Canopy processes
2. Involve Canopy people to participate in the system
3. Start managing Client (and Supplier) relationships




Figure 2 Implementation Steps

This proposal focusses primarily on Step-1 as this was indicated as a priority need for Canopy, Step-2 and 3 are only briefly described and can be expanded upon at a later stage.


2.1 Step-1:

2.1.1 Initiate:

Senority will make an Evaluator environment available to Canopy. During the initiate phase, we will tailor the Senority best practices to the Canopy needs.

2.1.2 Process Support:

The immediate need is to support the existing Canopy processes in a uniform way where defined business rules need to structure the management information enabling not only real-time online dash-boards and reporting, but also actively manage the numerous teams, members and their actions in an efficient way.

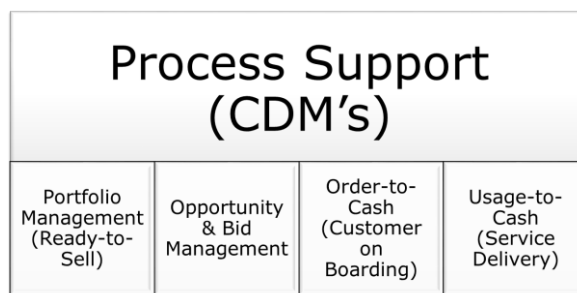

2.1.3 Integration:

During the Process Support implementation we will determine the need for interfaces and/or import utilities to facilitate consolidation of information originating from Canopy or other (Atos) systems into Evaluetor. Priorities and specifications will be determined during the Process Support phase and these Change Requests will be priced using the agreed rates (see 5.3 Support and Development Services.).

The Integration activity is aimed at integrating Evaluetor further in the Canopy toolset thus realizing the necessary interfaces between these tools and the Evaluetor result-connectors. The information to make accurate estimates for this activity is currently not available. Senority proposes to make an estimate for each integration need on a case by case basis.

2.2 Step-2:

As a next step, Evaluetor can be rolled out to the people that participate in the main processes. Senority will be available to assist Canopy with implementation support, training, process optimisation and change management aspects of this important step. This is where the additional benefits of management control, transparency and improved communication become visible throughout the organisation.

2.3 Step-3:

The ultimate goal is to also collaborate with the Canopy Clients and achieve superiority in client satisfaction, and add-on business while achieving maximum return on your existing contract base.

Making use of all the functions of Evaluetor will help Canopy to:

- Excel in customer satisfaction and retention;
- Grow with existing clients;
- Improve their new business “fit-to-Portfolio”
- Increase return on contracted Services;
- Decrease operational cost by assuring quality of contract delivery.

Senority is convinced that Canopy will make significant progress on these objectives. The sooner the roll-out of Evaluetor to the strategic accounts of Canopy takes place, the sooner the more substantial benefits in these areas will materialize. We are confident that the implementation of Evaluetor will distinguish Canopy in the market as a prime example of a client driven service organisation that strives for mutual sustainable and beneficial relationships with its clients.

Senority can make its experienced consultants available to support Canopy with this roll-out.

3. STEP-1: program Implementation structure.

The structure of the implementation program assumes that first the main Canopy Processes will be enrolled into Evaluetor. After operationalising this for the CDM organisation we can gradually involve the other stakeholders and make them participate in the processes.

3.1 Planning of Step-1.

The below planning works toward a gradual implementation that starts with some preparation activities where we make the system available to Canopy and ensure that generic setting are most aligned with the Canopy standards. We will implement support for the main Canopy process one by one. First we will work with Canopy staff to determine the requirements for that process, seek agreement and then execute the actual population of information in the related Evaluetor functions. During this period we will also determine the need for interfacing of import rules which we can develop and implement during the Integration phase.

Canopy Evaluetor Planner

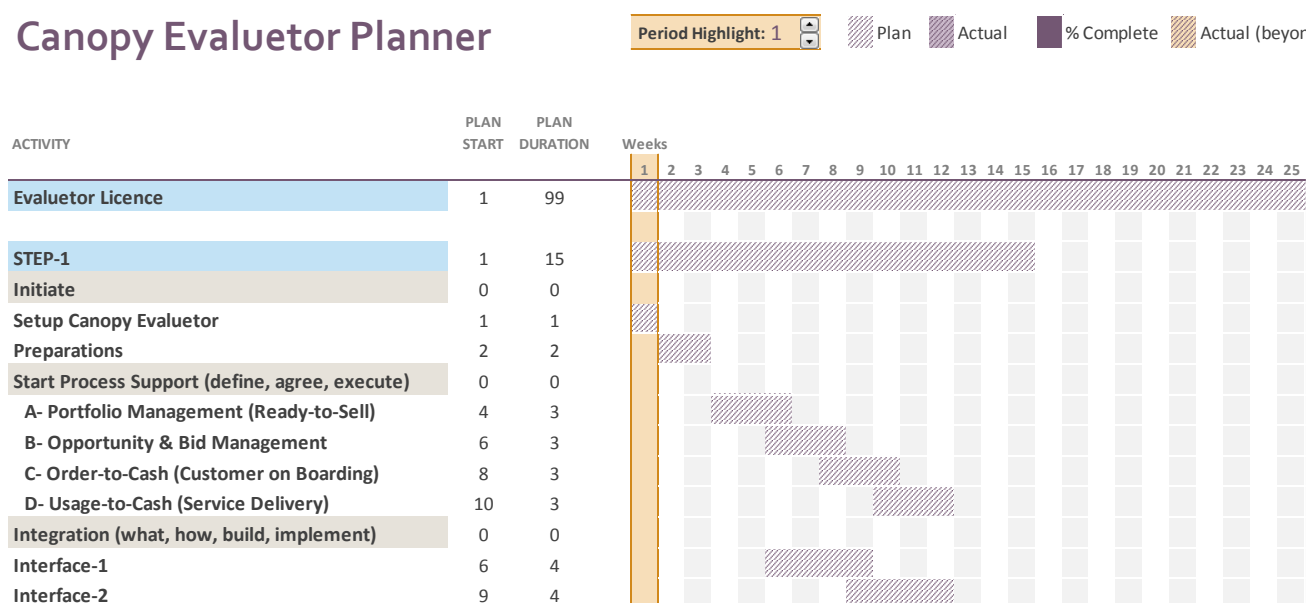


Figure 3 High Level planning of STEP-1

3.2 Set-up Canopy Evaluetor.

Based on the Canopy organisation and various user groups, a dedicated Canopy site collection will be created in Evaluetor. Several views, such as management views, account views, client views, governance team views, etc. will be accommodated. Based on the defined views, sites will be created to accommodate the various user groups. These sites assure that users will only have to interact with those parts of Evaluetor that are relevant to their function and their authorisation level. We will also define the Canopy organisation and users in the service and agree on several base parameter settings in Evaluetor.

The main deliverables of this activity are:

- Site collections defined based on views specification;
- Organisation structure, officers and users defined in Evaluetor;
- Standard parameters validated and set in Evaluetor;
- Infrastructure connectivity between Canopy and Evaluetor established.

3.3 Preparations.

The Evaluetor service comes with Senority's best practices. The objective of this activity is to validate Senority best practices against existing practices of Canopy and any requirements Canopy might have for these practices. Based on the input, a Canopy specific process is agreed that can be fitted into Evaluetor.

Main deliverables of this activity are:

- User accounts;
- Introduction to Evaluetor and Key user training;
- Control cycle definition, frequency and set-up;
- Canopy user aids;
- Organising the Process support steps and priorities.

3.4 Process Support.

We will implement support for the existing Canopy processes in a uniform way:

1. Define specific requirements for this process
2. Agree on approach within Evaluetor
3. Execute the realisation of above in the operational system

This will result in real-time online dash-boards and reports where defined business rules are supported by Evaluetor functions. This will assist Canopy staff and management to actively manage the numerous team, members and their actions in an efficient way.

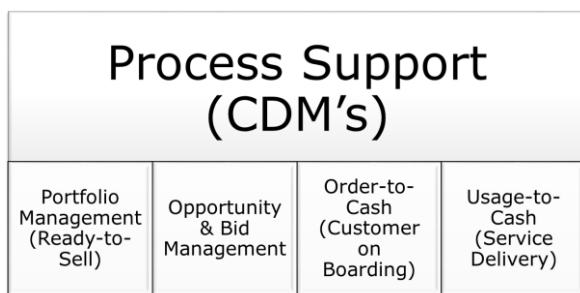


Figure 4 Canopy main processes

The Evaluetor Relationship, Service and Contract management functions including the improvement management process will be the building blocks with which we envision to create the foundation for the Canopy processes.

Main deliverables are:

- Key Stakeholder identified;
- Canopy employees trained;
- Services define in Evaluetor
- Initial client relationship scoring defined;
- Governance structure agreed and defined in Evaluetor;
- Commitment- and improvement plan monitoring cycle defined;
- First commitment and improvement plan monitoring cycle completed.

Summary of business functions needed per main process:

Portfolio Management	Opportunity & Bid Management	Order-to-Cash	Usage-to-Cash
Define and maintain checklist	Maintain list of opportunities	Define and maintain checklist	Register monthly service level returns
Assign tasks to action owners	Automatic import of opportunities from external source	Assign tasks to action owners	Report service level returns and history
Maintain deadlines	Maintain sales status of opportunities	Maintain deadlines	Register overall service status per customer and define management escalations
Maintain status of activities	Validate deviations from standard product	Maintain status of activities	Provide real time status of service per customer to senior management
Keep management informed	Maintain list of Canopy supporting sales actions	Keep management informed	Create views per product group (IaaS, PaaS, SaaS)
Use template checklist to copy per Ready-to-Sell project	Assign supporting actions to action owners	Use template checklist to copy per Ready-to-Deliver project	
Maintain Service Portfolio	Maintain status of list of supporting actions	Maintain overall ready-to-deliver status for management reporting	
Maintain Service Portfolio versions	Link Opportunity to service portfolio product	Checklist dashboards	
Maintain Service Level definitions	Define important product standards for deviation and risk checking		
Maintain product data such as product sheets	Define customer contract		
Create views per product group (IaaS, PaaS, SaaS)	Define important contract commitments to monitor		
	Transfer signed contract to O2C list		

3.5 Integration

During the creation of the implementation of the process support functions, the need for interfaces to further integrate Evalueter in the Canopy environment will be identified. We propose to do this using the What, How, Build, and Implement approach on an as needed basis which can be flexible in time.

From the information gathered during process support implementation we determine what needs to be optimised. Senority will then investigate how this can be done best and at which cost. After Canopy approval for the Change Request the solution will be built and tested. When the solution is functionally accepted by Canopy, Senority will make this available in the Canopy Cloud.

3.6 Implementation Support

A successful Evalueter implementation requires a clear commitment from the Canopy management team. Contract management, relationship management, and improvement management will benefit from a structured approach with exemplary management behaviour and communication. Since this is a client transparent process, it is imperative that implementation should be flawless.

Senority is well suited to provide change management support to assist Canopy management with this task and to ensure maximum results can be obtained with optimised efforts. A range of C-level and Account level reports are available to assist management with this task. An experienced Senority implementation manager would be assigned to assist Canopy during the initial steps or throughout the entire rollout period if so desired.

3.7 Program Governance Structure

In order to assure a controlled program implementation, Senority and Canopy require a clear Governance structure. Senority advises to have 3 types of Governance bodies:

- A program steering group;
- A project work group;
- Account implementation work group. **(only during Step-3)**

Governance team	Program Steering Group
Goals and Objectives	The program steering group is responsible for value management of the project, monitor project cost and project progression. The steering group also assures commitment from the organisation and has an important responsibility in the communication internally, to the clients and to the market about the program.
Participants	Canopy COO (Karl Deacon) on request
	Canopy BTN VP Sales (Enrico de Boer)
	Canopy CDM Lead (Koos van den Berge)
	Senority Project Lead (T.B.A.)
	Senority Managing Partner (Steven Visser)

Governance team	Project Work Group
Goals and Objectives	The project work group is responsible for producing all deliverables that are not account specific. The project work group decides on business processes, standard KPI's, sequence of account implementations, integration with Canopy practices, and support staffing. The project work group is also responsible for stakeholder management for the program
Participants	Canopy CDM Lead (Koos van den Berge)
	Senority Project Lead (T.B.A.)
	TBA
	TBA

Governance team	Account Implementation Work Group
Goals and Objectives	Account implementation work groups assure the effective implementation of Evalueter at the account level. The account implementation work group is responsible for entering Account data in Evalueter, such as contract data, assure account officers understand and execute the tasks that they have to perform at the account level and assist the Canopy Client to select officers to contribute in the process and assist the Canopy Client in the effective implementation.
Participants	Canopy Account Manager
	Canopy Implementation Lead (PMO t.b.a.)
	Senority Implementation Manager

Account Implementation work groups are only active during “Step-3” the implementation for a specific client account.

4. Step-1 Time estimates and assumptions.

Evaluator is offered as a cloud service using registered user subscription model with a minimum of 50 subscriptions. The implementation effort from Senority is offered on a time and material basis. In order to provide an indication of the associated cost to Canopy, Senority has done a best effort estimate of the various activities of the rollout plan:

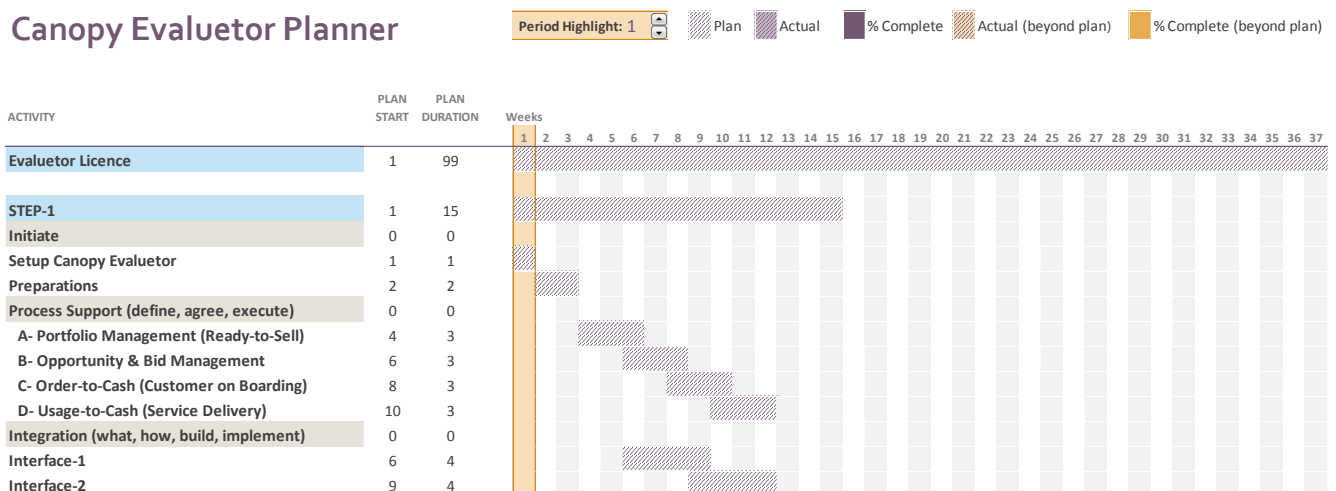


Figure 5 High Level Planning

4.1 Estimating and costing assumptions.

Senority has used several assumptions for the estimates which are presented below. The following assumptions were used:

- The Canopy CDM organisation will initially use Evaluator to administer and coordinate all named Canopy accounts;
- Canopy will rollout relationship management, contract management and improvement management functionality to all accounts;
- Canopy will assign an Evaluator administrator / Key User during the Initiate phase of the project, thus positioning to diminish the dependency of Senority for subsequent activities;
- Senority expects generic change management support to be necessary 2 days a month during phase-1;
- During the Process implementation we will have at least 1 day per week availability of CDM expertise (Koos van den Berge);
- Working location for the project is assumed to be either the Utrecht Canopy office or the Rotterdam Senority office;
- Additional travel and expenses are excluded.
- The Evaluator standard terms and conditions will apply.

4.2 Progress reporting and hour administration.

Since the implementation activities are on a time and material basis, Senority will provide monthly status reports with actual time spent per activity per role and the progress of the activity compared to the estimates provided in this proposal. These status reports provide insight for Canopy in actual versus estimated cost of the program.

4.3 Step-1 Time and cost estimates per activity.

This paragraph contains the time and cost estimates for the different implementation components of this proposal. The estimates for each of the separate activities are planned in days of work. The time estimates are separated for the different implementation roles of Senority. In order to arrive at the cost estimates, the roles and tariffs as mentioned in 5.3 Support and Development Services have been used.

The estimated Canopy implementation effort is provided in the table below:

Activity in Days	Implementation Consultant	Project Manager	Enhancement Developer	Evaluator	Administration	Estimated Cost	Estimated Canopy effort
STEP-1					0		
Initiate					€ -		
Setup Canopy Evaluator		4			€ 5.600,00	1	
Preparations	2	3			€ 7.600,00	2	
Process Support (define, agree, execute)					€ -		
A- Portfolio Management (Ready-to-Sell)	1	8			€ 12.900,00	3	
B- Opportunity & Bid Management	1	8			€ 12.900,00	3	
C- Order-to-Cash (Customer on Boarding)	1	8			€ 12.900,00	3	
D- Usage-to-Cash (Service Delivery)	1	8			€ 12.900,00	3	
Integration (what, how, build, implement)	1	2			€ 4.500,00	2	
Interface-1		0	0		€ -		
Interface-2		0	0		€ -		
Sub-Total Step-1	7	41	0	0	€ 69.300,00	17	

All cost estimates are exclusive of V.A.T. , travel and Expenses.

All above mentioned time- and cost estimates are one-off and non-recurring. Actuals can differ based on level of effort done by Canopy itself, speed of implementation and management commitment.

4.4 Consideration for the number of Canopy Evaluator subscriptions

The actual number of subscriptions needed depends on several factors. Most important is the number of key people that contribute to a client relationship, both from Canopy and the client side. Typically, large accounts have more key contributors than small accounts.

Key personnel for an account include, but are not limited to:

- Client Executives;

- Client Delivery Executives;
- Engagement managers;
- Service delivery managers;
- Executive Sponsors (client user);
- Contract managers (client user);
- Service level managers (client users).

Next to the users that are directly involved in a client relationship, a number of other Officers will require access to the service, such as:

- Canopy Management Team
- Business development;
- PMO;
- Service Line managers;
- Legal;
- Finance.

Rule of thumb is that a large account requires 15-20 seats and smaller account suffice with 5-7 seats.

These estimates can be refined as we gain more insight in the organisational structure of Canopy and the governance structures used with the Clients. For instance, when a Client Executive is responsible for 3 clients, he will need only one (1) Evaluator subscription.

5. Evaluator User Subscription fees and Rates.

5.1 Evaluator Cloud Services.

Senority will make User Subscriptions effective for the following Services, all prices are exclusive of V.A.T.:

Nr.	Description	# Users	Monthly Fee
1.	Base subscription Evaluator Cloud Services - Contract Management - Relationship Management - Service Management - Improvement Management	50	€5.000,-
2	Additional user in addition to Base users	1	€75,-

5.2 Storage Fees.

Next to the User Subscription fees, charges might become applicable for use of storage according to the table below. Each User Subscription has 1 GB Storage available to store your data, this storage will come available as one (1) storage pool where this storage will be shared amongst all users. Only when this total storage pool is exhausted additional storage charges will apply.

Nr.	Description	GB	Monthly Fee
1.	Initial Storage per User (included in Service Fee)	1	€0,--
2.	Additional Storage	1	€ 2,50

5.3 Support and Development Services.

During the Evaluator project Canopy may from time to time require Implementation or Enhancement support from Senority. Such activities would be jointly agreed as additional projects or on a time and material basis.

Nr.	Description	Day Rate
1.	Implementation Consultant	€ 1.700,--
2.	Project Manager	€ 1.400,--
3.	Evaluator Enhancement Developer	€ 1.200,--
4.	Evaluator Administration	€ 950,--
4.	Car Travel allowance per kilometre	€ 0,40

The above-mentioned listed tariffs are excluding V.A.T., travel and expenses.

6. Appendix A - Short Description Evaluetor Functionality.

Evaluetor is an integrated Cloud service that clients can subscribe to. Clients pay for the subscription in monthly fees per registered user. The service can be accessed through the Internet using an Internet browser. Senority provides application and user support on the service.

The functionality of Evaluetor consists of 7 main building blocks:

- Relationship Management;
- Contract Management;
- Service Management;
- Improvement Management;
- Risk Management;
- Opportunity Management;
- System Administration functions.

When subscribing to Evaluetor, clients can obtain the full functionality of all the building blocks. Every implementation of Evaluetor requires a client specific set-up, depending on the organisation of the client and the way in which the service will be used. The service is made available through web-based access. Standard part of the implementation is a client specific set-up of site collections and client specific parameters. Evaluetor functions can also be configured to the specific needs of a customer. Evaluetor is flexible as to which functions can be combined on an Evaluetor function page.

6.1 Relationship Management.

The Relationship Management service enables Canopy to define relationship KPI's with strategic clients and/or suppliers. These KPI's provide additional ways to measure the health of a relationship, alongside already used Service Performance Indicator's as defined in Service Level Agreements or Statements of Work.

Both key officers of Canopy and their clients can score these KPI's at self-chosen intervals. Evaluetor allows the parties to compare the KPI scores and summarize them in a provider- and a client summary. Based on the scores and comments provided, improvement actions will be defined to bring the relationship at a higher level.

6.2 Contract Management.

The Contract Management service enables Canopy to create new contracts and upload existing contracts. Evaluetor enables relationship owners to define commitments in their own words and relate them to the relevant contract documents and contract clauses. Deadlines for commitments can be defined and alerts can be set to warn for key moments and events in the contract. Conditions under which commitments might be triggered can also be defined and maintained in Evaluetor.

Defined commitments can then be assigned to governance teams for the purpose of monitoring. A monitoring cycle can be defined (weekly, monthly, etc.) which allows the partners to use status updates to monitor the progression of the commitments.

Each governance team can have a dedicated site where all the relevant information on the commitments

comes together and status updates can be viewed. This allows the Governance team to be on top of all manageable commitments and define and monitor any necessary improvement actions.

6.3 Service Management.

The Service Management service enables Canopy to maintain their portfolio of services and score Service Performance Indicators (SPI's). Evaluetor allows Canopy to define its service portfolio and link contracted services to the portfolio. By doing this in a consistent way, Canopy can obtain a horizontal view of how well services are received by accounts and clients and compare the SPI's.

Evaluetor will be able to collect and report traditional service level returns, but the intent of the SPI's is to collect more qualitative- and opinion based information on the services alongside traditional service level returns.

By using Service Management, Canopy will bring service units in closer contact with account- and client opinions.

6.4 Improvement Management.

The Improvement Management service enables Canopy to define and monitor any improvement actions that are defined for its clients. Improvement actions can be defined and included into a monitoring cycle. Action owners will be assigned and they can make frequent status updates on the improvement actions. Actions are linked to Governance teams that are responsible for managing the improvement action. Governance teams can view both commitment- and improvement actions as part of their responsibility.

Improvement management allows Canopy to implement a structured process of continuous improvement that is shared and transparent to the client. Improvement management reduces the dependency on email based communication and informal promises.

6.5 Risk Management.

The risk management functionality allows Canopy to maintain a risk profile on contracts and the promises made. The risk management information is not automatically shared with the client and allows Canopy to evaluate and manage its own risk profile in the contract.

The risk management functionality allows Canopy to define its own standard contract policies and register deviations to the standard and manage the associated risk.

6.6 Opportunity Management.

Evaluator has an Opportunity Management service where opportunities for prospects can be maintained and monitored. Opportunities can be tracked through the different sales stages of a sales cycle.

When it is time to close a contract, Evaluator allows the sales team to define requirements for the contract and monitor the resolution of these requirements during negotiations. This is the linking pin with the contract management functionality of Evaluator, where the requirements eventually end up as commitments in a contract. This allows for a structured and qualitative handover from the sales team to the account team during turn over to production.

6.7 System Administration.

Evaluator has several central functions that are necessary to facilitate its business. This includes but is not limited to:

- Defining legal and organisational structures;
- Defining new partner relationships;
- Maintaining officers;
- Maintaining governance teams and governance team members;
- User administration;
- Document library maintenance.

6.8 Management Reporting.

Evaluator comes with a predefined set of management reports. The reports are integrated in the various sites and easily accessible to the users. Management reports provide sorted and targeted management information that allows the organisation to stay on top of the value, risks and benefits of strategic relationships.
